


# TEYNHAM PRIMARY SCHOOL

## WEEKLY PROGRESS UPDATE

### 06.05.2025

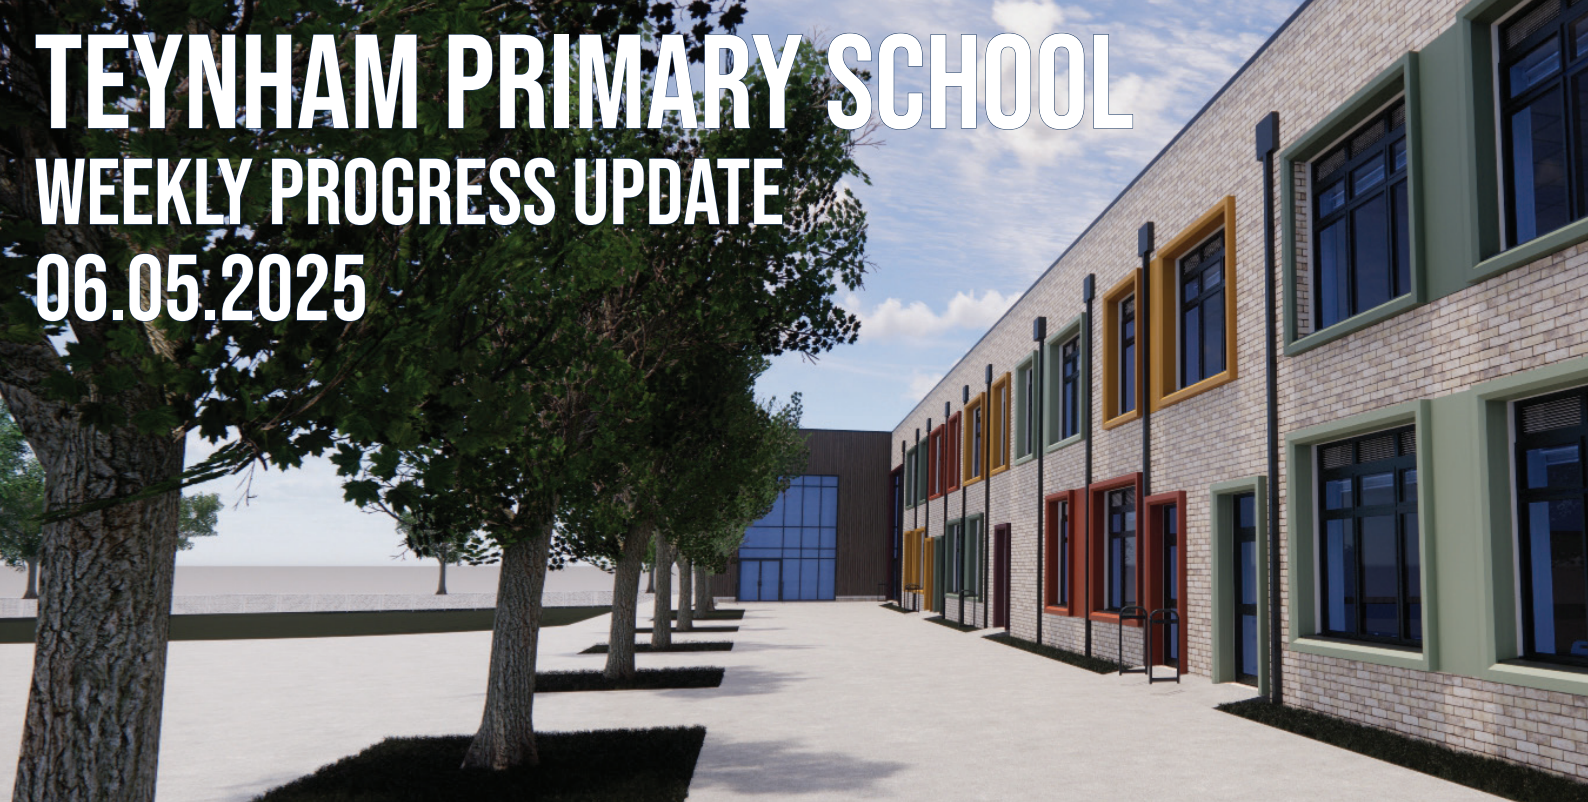

We are pleased to share the latest update on progress at Teynham Primary School. This week has seen significant developments both internally and externally as we move closer to project completion.

#### **Mechanical and Electrical Works**

Mechanical second fix works are continuing, with water boilers now being connected in kitchen units and classrooms. The kitchen extract canopy and ductwork have been fully installed. Electricians remain on site carrying out second fix installations, including fitting the data cabinet, switches, and dado trunking across the building. Hall lighting has now been completed.

#### **Internal Finishes**

All ceilings have now been installed throughout the building. Acoustic panels have been successfully fitted to the walls in the hall, and splashbacks have been installed in the toilets, kitchenettes, and staff room. Decoration works are progressing well, with the topcoat now completed on the first floor and ongoing work to rooms and woodwork on the ground floor. A builders' clean has now commenced on the first floor.

#### **Fire Safety and Joinery**

Sprinkler installations are continuing, with sprinkler heads now fitted to ceilings throughout the building.

Final fix works have begun to internal doors and joinery screens on the ground floor. Teleflex window closers have also been installed.

#### **Classroom and Kitchen Fittings**

Classroom kitchen units have now been fully installed. The Food Technology kitchen fitting is nearing completion.

#### **External Works**

Ground levels around the new school building have been built up and prepared for surfacing. Tarmac has now been laid, and the soft play area for Reception and Nursery children is complete.

Planters have been installed within the play area, enhancing the new outdoor space. Work continues on installing external ducts for future phases of the project.

#### **Façade and External Installations**

Window surrounds and cladding panels are now complete on all elevations. The Broxap canopy has been installed at the front elevation, marking another visual milestone in the project.

#### **Site Security and Setup**

Our 24-hour CCTV monitoring system remains in place to ensure site security. The relocation of the site setup has been completed, including the repositioning of perimeter fencing and cabins.

#### **Utilities and Power Supply**

UKPN works to Station Road have now been completed, with the substation made live and supplying power to the new school building. Final water connections have also been successfully completed by Waterlink.

A drone visit was carried out this week to document external progress and we look forward to sharing the images in due course.

We thank you for your continued support as we progress through these final stages of construction.







